

# V/Line – Completion Report



**Project:** 2588 - V/Line DBKWDG Access Track Summerhill Rd to Donnybrook Rd

**Customer:** V/Line

**PO / LOE:** 194193

**Location:** Donnybrook, VIC (KP – )

**Status:** Completed

**Date Completed:** 2025-07-03

- **Work Description:** Multi Tiered works in this area over 7 working Days. Including Manual Hand Cutting with Brushcutters. Tree Trimming ELC Works at DonnyBrook Rd Crossing Private owned trees trimming aver 1500mm from open Low Voltage Conductors. Mulching of vegetation under Pole Lines with 3 items of Equipment Kubota 5t Excavator with Sepi. H3 Mulcher. KUBOTA SVL95 with FAE Mulcher and New Seppi 1700 Forestry Mulcher after damage received to FAE Mulchers from contacting Railway Line debris hidden in ground. Also used is the JCB hyradig with Seppi HD Forestry Mulcher. Has resulted in all areas outside significant vegetation zones fenced off all Gorse, Blackberry and English Broom mulched to ground. All trees and previously removed trees also actions for ELC maintenance. Started project 19th May 2025. Had delays with machinery damage. Re commenced and completed all works June 23, 2025...
- **Scope of Works:** Cleared everything possible from poles, powerlines and in the easement.
- **Date of Works:** 2025-05-19 to 2025-06-23
- **Vegetation Mulched:** Yes

## Summary

Vegetation management and ELC trimming were successfully carried out between Summerhill Rd and Donnybrook Rd in Donnybrook. The project involved both manual and mechanical clearing, mulching, and tree trimming to ensure safe clearances around powerlines and within the easement. All areas outside significant vegetation zones were effectively addressed.




## Key Findings

- Vegetation and tree trimming completed along the access track and easement.
- Manual and mechanical mulching addressed Gorse, Blackberry, and English Broom.
- Private trees near low voltage conductors trimmed to maintain clearances.
- All areas outside significant vegetation zones were fenced and cleared.
- Machinery damage caused delays, but all works were completed by 23 June 2025.

## Media

### Before

### During

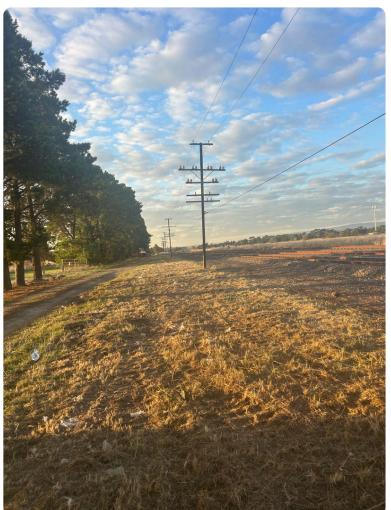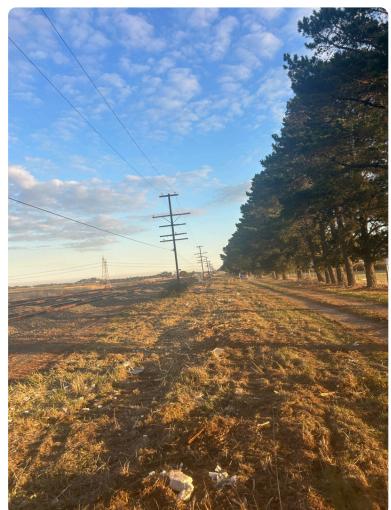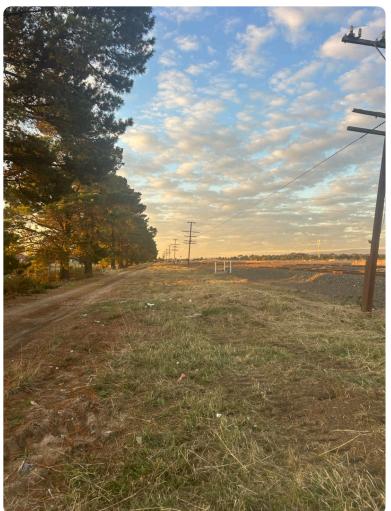

**After**



Generated by **Systems @ TMC enviro**

[www.tmcenviro.com.au](http://www.tmcenviro.com.au)

Email: [systems@tmcenviro.com.au](mailto:systems@tmcenviro.com.au) | Phone: +61 458 922 033
